Diving Into Technology

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

Technical & Financial Proposal

'X' Legal Platform – Website, Client Portal & Admin Portal Development Project

Prepared by: Riseup Labs

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

1. Introduction

This document presents the technical and financial proposal for developing the 'X' Legal Platform as a from-scratch digital solution covering the public website, Client Portal, and Lawyer/Admin Portal. The proposal is prepared based on the Development Project Charter and focuses only on development scope, related implementation activities, quality assurance, deployment readiness, and handover.

Key proposal conditions:

- Scope is limited to development only. UI/UX design creation is excluded and implementation will follow the approved design reference provided by the client.
- The platform will be built from scratch with a modular architecture to support future enhancement without rework of the core foundation.
- The implementation will cover bilingual support for English (LTR) and Arabic (RTL), as explicitly required in the project charter.
- Third-party subscription or usage costs such as hosting, payment gateway charges, WhatsApp API charges, SMS, email service, and domain-related fees are excluded and will be paid directly by the client.
- Any requirement beyond the approved scope will be handled through a formal Change Request process.

2. Project Understanding & Objectives

The target platform is a premium LegalTech solution intended to digitize legal service delivery into a structured, user-friendly, and operationally manageable system. Based on the project charter, the platform must support three core service models: Instant Contracts, Fixed-Price Legal Services, and RFQ-based Custom Legal Services. It must also provide an end-to-end customer journey from service discovery to request submission, payment, document handling, tracking, and post-purchase communication.

- Develop a high-performance responsive website for service discovery, conversion, and multilingual presentation.
- Provide a secure Client Portal for account access, request tracking, documents, communication, and payment follow-up.
- Provide a secure Lawyer/Admin Portal for operational control, service configuration, request handling, quote management, and multilingual content management.
- Integrate one payment gateway(mada/Stripe), WhatsApp notifications, email notifications, and basic analytics in line with the charter.
- Deliver production-ready source code, repository setup, deployment readiness, and technical documentation.

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

3. Proposed Technical Approach & Methodology

We propose a modular web application architecture with a decoupled frontend and backend. The public website and user-facing portal interfaces will be implemented using Next.js using performance, and strong multilingual support. The backend will be implemented using NestJS on Node.js with PostgreSQL as the transactional database. This approach supports clean API separation, secure role-based access, easier maintenance, and future scalability.

3.1 Development Methodology

- Requirement-aligned phased delivery with formal review at the end of each phase.
- From-scratch implementation using reusable components and API-first backend design.
- Staging-based validation before production release.
- Role-based access, secure file handling, and environment-based configuration as standard engineering controls.
- Progressive QA coverage includes functional testing, integration testing, responsive testing, and support.

3.2 Suggested Technical Stack

Layer	Proposed Technology
Frontend	Next.js (React) with TypeScript
Backend	Node.js with NestJS
Database	PostgreSQL
Authentication	JWT / secure session strategy with role-based access
File Storage	Cloud storage compatible with GCP deployment
Hosting / Deployment	Google Cloud Platform (GCP)
Notifications	WhatsApp API and transactional email service
Payments	Client-provided one Saudi payment gateway with Mada support
Analytics	Google Analytics (basic event and conversion tracking)
Project Tools	GitHub/GitLab, ClickUp, Slack/Gmail

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

4. Three-Phase Scope Breakdown

To control delivery risk and ensure structured implementation, we propose breaking the development scope into three phases. Each phase has a focused deliverable set, estimated timeline, and resource participation aligned with the project charter only.

4.1 Phase 1 – Core Platform Foundation & Public Website

This phase establishes the technical foundation and develops the public-facing website experience required for service discovery and user onboarding.

- Project setup, environment configuration, repository setup, branching strategy, and deployment pipeline baseline.
- Frontend foundation with responsive implementation, bilingual structure, RTL/LTR handling, shared layout components, and reusable UI components.
- Public website pages: Homepage, Services Listing, Service Detail pages for all three service types, About Us, Contact Us, FAQ/Help, legal pages, and authentication pages.
- Core website browsing features such as categorized service display, filtering, CTA-driven flow entry points, and SEO-ready page structure.
- Backend foundation including database schema, API structure, authentication baseline, user role model, multilingual content model, and media/file management setup.
- Phase 1 Human Resources & Responsibilities

Role	Short Responsibility
Project Manager	Planning, coordination, milestone tracking, and client communication
Product Designer	Requirement clarification, scope control, and acceptance alignment
Tech Lead	Architecture setup, technical decisions, and code review
Frontend Developer	Responsive website pages, component development, and multilingual frontend implementation
Backend Developer	API foundation, database schema, authentication, and content/service models

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

QA Engineer	Functional test preparation, responsive checks, and initial regression coverage
DevOps Engineer	Environment setup, CI/CD baseline, staging deployment support

4.2 Phase 2 – Client Portal & Transactional Service Flows

This phase delivers the logged-in client experience and the main transactional workflows that convert website visitors into active service users.

- Client Portal pages: dashboard, My Requests / Services, Request Details, Documents & Files, Messaging / Communication, and Profile & Settings.
- Instant Contract Generator with multi-step question flow, progress indicator, dynamic contract preview, and document generation support.
- Fixed-Price Service flow with service-specific forms, file upload, and payment initiation.
- RFQ service flow with case submission, document upload, request creation, and tracking initiation.
- Quote handling flow in the client portal including accept, reject, and payment actions.
- Integration of payment workflow, email notifications, and event-based WhatsApp notifications for approved use cases.

Phase 2 Human Resources & Responsibilities

Role	**Short Responsibility**
Project Manager	Phase tracking, dependency management, and review coordination
Product Designer	Validation of portal workflow, field logic, and business rule clarification
Tech Lead	Transactional flow review, integration approach, and architecture governance
Frontend Developer	Portal UI implementation, wizard flow screens, and payment-related frontend integration
Backend Developer	Portal APIs, request workflow logic, document handling, messaging, and payment/notification integration

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

QA Engineer	End-to-end flow testing for contracts, fixed-price service, RFQ, and notifications
DevOps Engineer	Service configuration, secure environment variables, and staging support for integrations

4.3 Phase 3 – Lawyer/Admin Portal, Final QA, Deployment & Handover

This phase completes the internal operational system and prepares the full platform for production launch and formal handover.

- Lawyer/Admin Portal pages: Admin Dashboard, Request Management, Service Management, Contract Template Management, User Management, Messaging System, and System Settings.
- Operational features including status updates, service creation and pricing control, quote generation, role and permission management, multilingual content control, and internal communication support.
- Basic analytics integration finalization with page tracking, user behavior tracking, and key conversion tracking.
- End-to-end QA, bug fixing, QA support, production deployment readiness, and repository/documentation handover.
- Technical documentation including setup guide, environment configuration reference, and API documentation.

Phase 3 Human Resources & Responsibilities


Role	Short Responsibility
Project Manager	Final delivery governance, sign-off coordination, and release planning
Product Designer	QA coordination, change log review, and handover alignment
Tech Lead	Final technical review, deployment sign-off, and code quality oversight
Frontend Developer	Admin portal interface completion and final frontend issue resolution

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

Backend Developer	Admin modules, role/permission logic, analytics integration, and documentation support
QA Engineer	Full regression, browser/device coverage, defect validation, and release readiness checks
DevOps Engineer	Production deployment support, release checklist, and handover of environment references


5. Recommended Diagram Placeholders

5.1 High-Level Solution Architecture




+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

5.2 Client Service Journey Flow

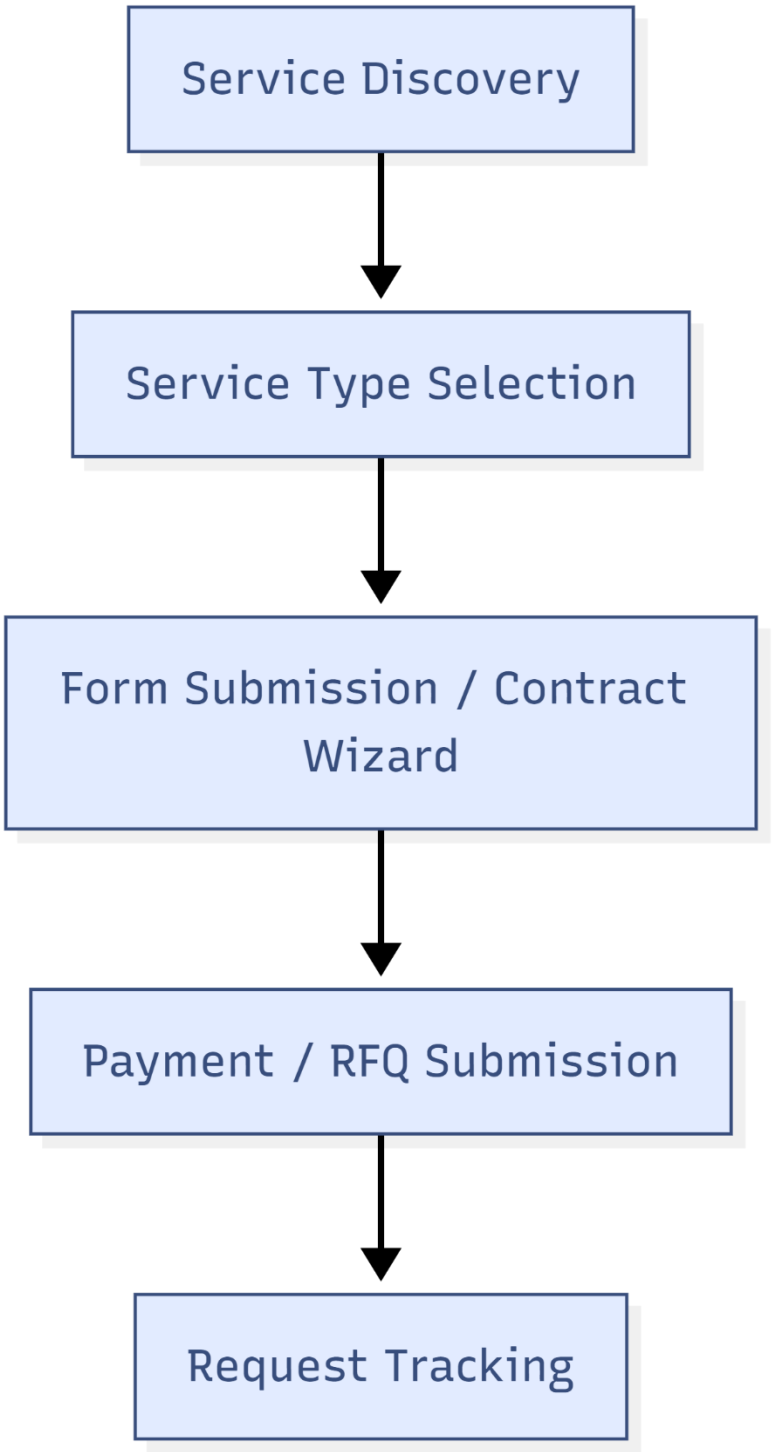

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

5.3 Placeholder 3 – Admin Request Handling Workflow

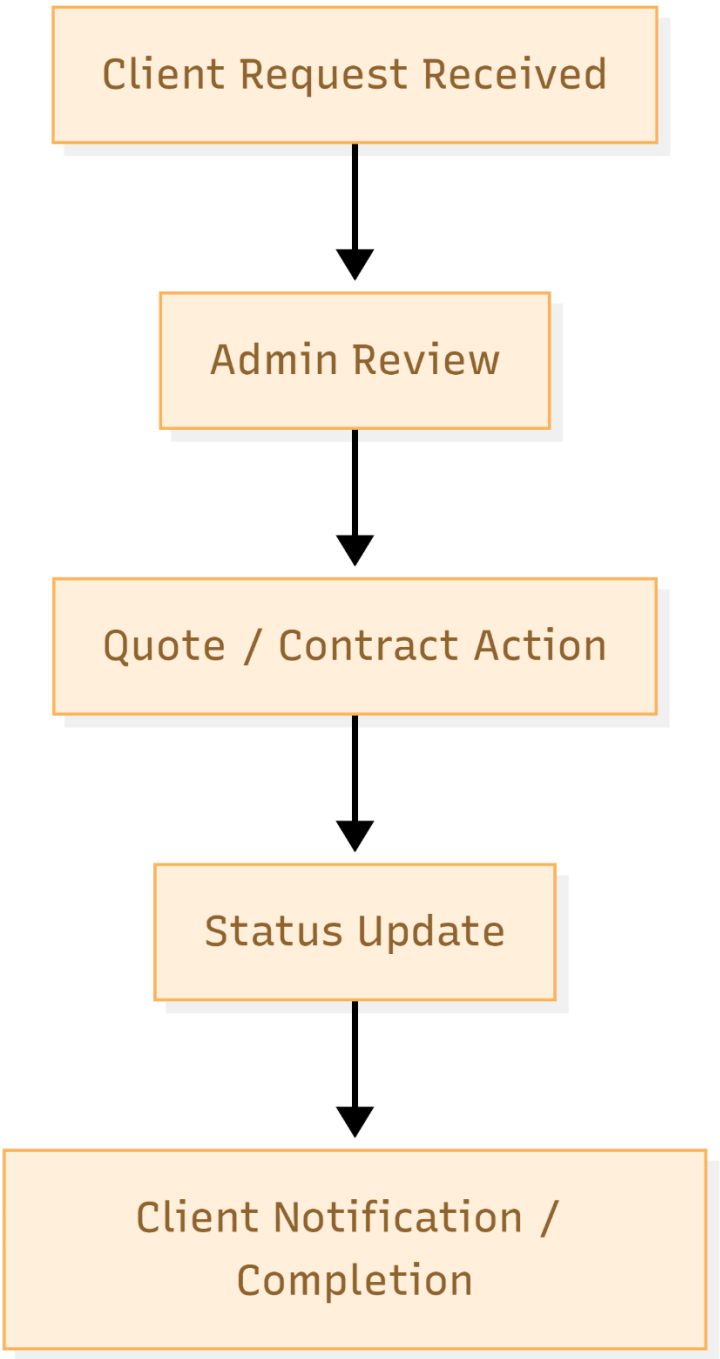

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

6. Testing, QA & Deployment Approach

- Functional testing across all major user journeys and admin actions.
- Cross-browser testing for Chrome, Safari, Firefox, and Edge.
- Responsive testing across mobile, tablet, and desktop breakpoints.
- Validation of bilingual rendering including Arabic RTL and English LTR behavior.
- Secure authentication, secure file handling, and role-based access checks.
- Staging validation before production deployment and support during QA sign-off.

7. Complimentary Support

One (1) month of complimentary post-launch support will be provided after production deployment and formal handover.

- Bug fixing for issues directly related to the delivered scope.
- Minor adjustments within the existing delivered workflow or configuration.
- Basic technical support for deployment-related clarification during the support window.

Excluded from complimentary support:

- New features, major enhancements, or workflow changes beyond the approved scope.
- Third-party provider policy changes or newly introduced charges from external services.
- New legal content drafting, translation work, or design changes not part of implementation.

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

8. Financial Proposal

The following estimate is prepared based on the current charter scope and a from-scratch development approach. It is a budgetary estimate for implementation only and excludes third-party service fees, hosting consumption, payment gateway charges, WhatsApp usage fees, and any client-side licensing costs.

Phase	Scope Summary	Suggested Timeline	Estimated Cost (USD)
Phase 1	Core platform foundation, bilingual public website, authentication baseline, backend setup	0.5 Weeks	$1200
Phase 2	Client Portal, contract generator, fixed-price service flow, RFQ flow, payment and notifications	2.5 Weeks	$2200
Phase 3	Admin Portal, analytics finalization, QA, deployment readiness, documentation and handover	1 Weeks	$1600

Total Estimated Cost: USD 5,000

8.1 Payment Terms

- 30% advance payment upon project kickoff and initiation of Phase 1.
- 30% payment upon completion and sign-off of Phase 1 deliverables.
- 30% payment upon completion and sign-off of Phase 2 deliverables.
- 10% payment upon completion of Phase 3, production readiness, and final handover.

8.2 Change Request (CR)

- Any requirement beyond the approved scope will be handled through a formal Change Request process.
- Commercial impact of the change request will be estimated separately based on effort, timeline, and technical impact.

9. Assumptions & Out of Scope

- Client will provide final approved UI design, branding assets, legal content, contract templates, service content, Arabic/English copy, and required third-party credentials.
- Single Payment gateway account, WhatsApp API account, email service account, analytics account, and hosting account will be provided by the client unless agreed otherwise.
- Data entry beyond agreed setup, bulk content migration, and legal drafting of contract language are out of scope.
- Any major integration not mentioned in the charter is excluded from this estimate.

+88-0175-974-7387
contact@riseuplabs.com
riseuplabs.com

- Extended maintenance and support after the complimentary one-month period will be quoted separately, if required.

10. Acceptance & Sign-Off

The project will be considered completed when the agreed phase deliverables are implemented, verified in staging, major agreed defects are resolved, the final source code and documentation are handed over, and formal client sign-off is received.
